[YOUR CONSULTANCY]

[Project name] Statement of Work

Statement of work (SAMPLE CONTENT: replace everything in [brackets] and the sample scope)

PREPARED FOR	[Client contact], [Client role], [Client Company]
PREPARED BY	[Your Name], [Your role]
DATE	[Date]
VALID UNTIL	[Validity date, e.g. 30 days from issue]
REFERENCE	[SOW-0001] / v1.0

Commercial in confidence. This document contains proposal terms intended solely for the named recipient.

1. Executive summary

This statement of work (SOW) sets out what [Your Company] will deliver for [Client Company], when, for what fee, and how [Client] will accept the work. It is written so that both sides can check, line by line, whether a deliverable is done.

Sample scope: redesign and rebuild the [Client] customer portal, migrate existing accounts and train the support team. Replace this paragraph with one that describes your own project in two or three sentences.

At a glance

- Scope: [one-sentence description of what is in scope].
- Out of scope: [list what is not included, e.g. hosting, content writing, third-party licences].
- Fixed fee per option, invoiced on milestones. Work starts on [start date].

2. Understanding of your needs

The points below record the objectives and constraints the parties have agreed. Edit each row to match your project.

Need	What we heard
Objective	[What the project must achieve, in the client's words]
Users	[Who will use the result and how many]
Constraints	[Budget, deadline, systems or compliance limits]
Success measure	[How both sides will know the project worked]

3. Approach and phases

Work runs in four phases. Each phase ends with a milestone that the client accepts, or rejects with written reasons, within five working days.

3.1 Timeline

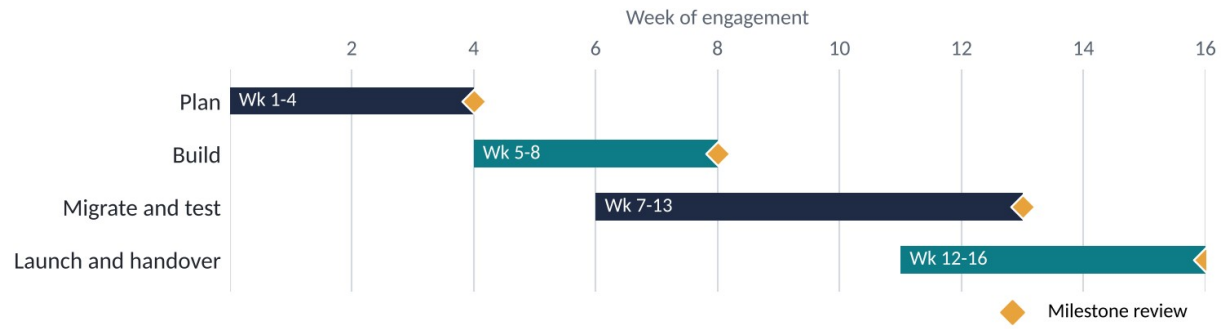


Figure 1. Indicative 16-week plan from kick-off. Diamonds mark milestone reviews.

3.2 Phase detail

Phase 1: Plan (weeks 1-4)

Agree requirements, plan and acceptance criteria.

- Kick-off workshop
- Requirements document
- Project plan and risk log

Milestone: Requirements signed off

Phase 2: Build (weeks 5-8)

Build the agreed scope in two-week sprints with a demo at the end of each.

- Sprint demos
- Weekly status note
- Test evidence

Milestone: Build complete

Phase 3: Migrate and test (weeks 7-13)

Move data, run user acceptance testing and fix defects.

- Data migration rehearsal
- User acceptance testing
- Defect fixes

Milestone: Acceptance testing passed

Phase 4: Launch and handover (weeks 12-16)

Go live, train the client team and hand over documentation.

- Go-live support
- Training sessions
- Handover pack

Milestone: Handover accepted

4. Deliverables

Each deliverable is accepted by the client's nominated owner at the milestone review for its phase. The Option column shows the lowest option that includes it.

Ref	Deliverable	Description	Phase	Option
D1	Requirements document	[Document listing agreed features; accepted when client confirms in writing]	Plan	Good
D2	Project plan	Timeline, owners and risks	Plan	Good
D3	Working [system or product]	Delivered to a test environment; accepted when all agreed test cases pass	Build	Better
D4	Data migration	[N] records migrated with a reconciliation report	Migrate and test	Better
D5	User acceptance test report	Pass/fail for each test case, with defects logged	Migrate and test	Better
D6	Go-live and training	[N] training sessions delivered; system live	Launch and handover	Best
D7	Handover pack and 30-day support	Documentation and fixes for defects found in the first 30 days	Launch and handover	Best

5. Assumptions and dependencies

The scope and prices in this document rely on the following. If any proves incorrect we will raise a change request before proceeding.

1. [Client] provides access to the systems and people named in this SOW within five working days of kick-off.
2. One named person at [Client] approves deliverables and answers questions within three working days.
3. Any work not listed in the deliverables is out of scope and handled through change control.
4. Third-party licences and hosting costs are excluded.
5. Delays caused by late client feedback move the dates by the same number of days.
6. [Add your own project-specific assumption.]

6. Pricing and options

We offer three options. All are fixed-fee for the stated scope. Better is our recommendation: it proves the benefit on live shipments before any wider commitment.

Scope	Core	Standard (recommended)	Full
Summary	Plan and build	Plus migration and testing	Plus launch and 30-day support
Requirements document and plan (D1, D2)	✓	✓	✓
Working system in test environment (D3)	✓	✓	✓
Data migration (D4)	–	✓	✓
User acceptance testing (D5)	–	✓	✓
Go-live and training (D6)	–	–	✓
Handover pack and 30-day support (D7)	–	–	✓
Duration	**8 weeks**	**12 weeks**	**16 weeks**
Fixed fee	**GBP 24,000**	**GBP 39,000**	**GBP 48,000**

6.1 Payment schedule

[Replace: for example 30% on signature, 40% on build complete, 30% on handover accepted.] Sample fees are placeholders; fees exclude VAT or sales tax and expenses.

[Prices are in GBP or USD; confirm currency and validity date.]

7. Terms and conditions

The clauses below are placeholders to be completed by each party's legal counsel before signature. Square brackets mark text that must be replaced.

Clause	Text
Acceptance procedure	[How deliverables are accepted or rejected, and the deemed-acceptance period - to be inserted]
Change control	[How scope changes are requested, priced and approved - to be inserted]
Payment terms	[Payment terms, e.g. net 30 days from invoice - to be inserted]
Intellectual property	[Ownership of deliverables and pre-existing materials - to be inserted]
Confidentiality	[Confidentiality clause or reference to existing NDA - to be inserted]
Governing law	[Jurisdiction and governing law - to be inserted]

8. Acceptance

By signing below, [Client Company] accepts this proposal and statement of work, including the option selected, and authorises [Your Consultancy] to proceed.

Option selected: [ ] Good [ ] Better [ ] Best

[Your Consultancy]	[Client Company]
SIGNATURE	**SIGNATURE**
NAME [Your Name]	**NAME**
TITLE Engagement Partner	**TITLE**
DATE	**DATE**
